

Carmichael Rec & Park Measure G
Program Schedule


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Timeline												
							Dec	Qtr 1, 2025 Jan	Feb	Mar	Qtr 2, 2025 Apr	May	Jun	Qtr 3, 2025 Jul	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec
52	Permitting	40 days	Tue 8/12/25	Mon 10/6/25	51														
53	Contractor Procurement	40 days	Tue 10/7/25	Mon 12/1/25	52														
54	Construction	70 days	Mon 3/9/26	Fri 6/12/26															
55																			
56	Carmichael Park - Vet's Hall ADA work (from WMB's 2020 estimate), Paving, Water Building/Records Storage-re-roofing (asbestos abatement), District Office-East Side Bldg. Roof, HVAC Clubhouse, Demo & Grading, Parking Lots, drive a	295 days	Mon 4/7/25	Fri 5/22/26															
57	Design	90 days	Mon 4/7/25	Fri 8/8/25															
58	Permitting	40 days	Mon 8/11/25	Fri 10/3/25	57														
59	Contractor Procurement	30 days	Mon 10/6/25	Fri 11/14/25	58														
60	Construction	90 days	Mon 2/16/26	Fri 6/19/26															
61	Bird Park - Demo & Grading, Playground Replacement, Rubberized surfacing, & ADA work	295 days	Mon 4/7/25	Fri 5/22/26															
62	Design	60 days	Mon 4/7/25	Fri 6/27/25															
63	Permitting	40 days	Mon 6/30/25	Fri 8/22/25	62														
64	Contractor Procurement	30 days	Mon 8/25/25	Fri 10/3/25	63														
65	Construction	90 days	Mon 2/16/26	Fri 6/19/26															
66																			
67	Series 3 Bond Projects	577 days?	Mon 4/13/26	Tue 6/27/28															
68	LA SIERRA (Funding based on location) - ADA improvements from 2016 report -Phase II, HVAC (Units TBD)	197 days	Mon 4/13/26	Tue 1/12/27															
69	Design	60 days	Mon 4/13/26	Fri 7/3/26															
70	Permitting	40 days	Mon 7/6/26	Fri 8/28/26	69														
71	Contractor Procurement	40 days	Mon 8/31/26	Fri 10/23/26	70														
72	Construction	57 days	Mon 10/26/26	Tue 1/12/27	71														
73																			
74	Carmichael Park (Tax Exempt) - Water Building/Records Storage-re-roofing (asbestos abatement), District Office-East Side Bldg. Roof, HVAC Clubhouse	308 days	Mon 4/13/26	Wed 6/16/27															
75	Design	70 days	Mon 4/13/26	Fri 7/17/26															
76	Permitting	40 days	Mon 7/20/26	Fri 9/11/26	75														
77	Contractor Procurement	40 days	Mon 9/14/26	Fri 11/6/26	76														
78	Construction	72 days	Mon 3/8/27	Tue 6/15/27															
79																			
80	Carmichael Park (Tax Exempt) - Demo & Grading, Parking Lots, drive aisles, and walkways	96 days?	Mon 4/13/26	Mon 8/24/26															
81	Contractor Procurement	40 days	Mon 11/2/26	Fri 12/25/26															
82	Construction	56 days	Mon 12/28/26	Mon 3/15/27	81														
83	Series 3 Bond Projects	210 days	Mon 3/1/27	Fri 12/17/27															
84	Patriots Park (Tax Exempt) - Demo & Grading, Playground, Rubberized Surface, Walkways ADA & ADA tables, Pedestrian Lighting, Site furnishings and accessories	200 days	Mon 3/1/27	Fri 12/3/27															
85	Design	60 days	Mon 3/1/27	Fri 5/21/27															
86	Permitting	40 days	Mon 5/24/27	Fri 7/16/27	85														
87	Contractor Procurement	30 days	Mon 7/19/27	Fri 8/27/27	86														
88	Construction	70 days	Mon 8/30/27	Fri 12/3/27	87														
89																			
90	Jan Park - Additional Playground equipment (inc: tot swings & misting stick), ADA improvements to existing areas (walkways, seating), Site furnishings and accessories	210 days	Mon 3/1/27	Fri 12/17/27															
91	Design	60 days	Mon 3/1/27	Fri 5/21/27															

Qtr 2, 2026 Apr | May | Jun | Qtr 3, 2026 Jul | Aug | Sep | Qtr 4, 2026 Oct | Nov | Dec | Qtr 1, 2027 Jan | Feb | Mar | Qtr 2, 2027 Apr | May | Jun

Project: Template_Schedule - A
Date: Wed 11/20/24

	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress		

**Carmichael Rec & Park Measure G
Program Schedule**

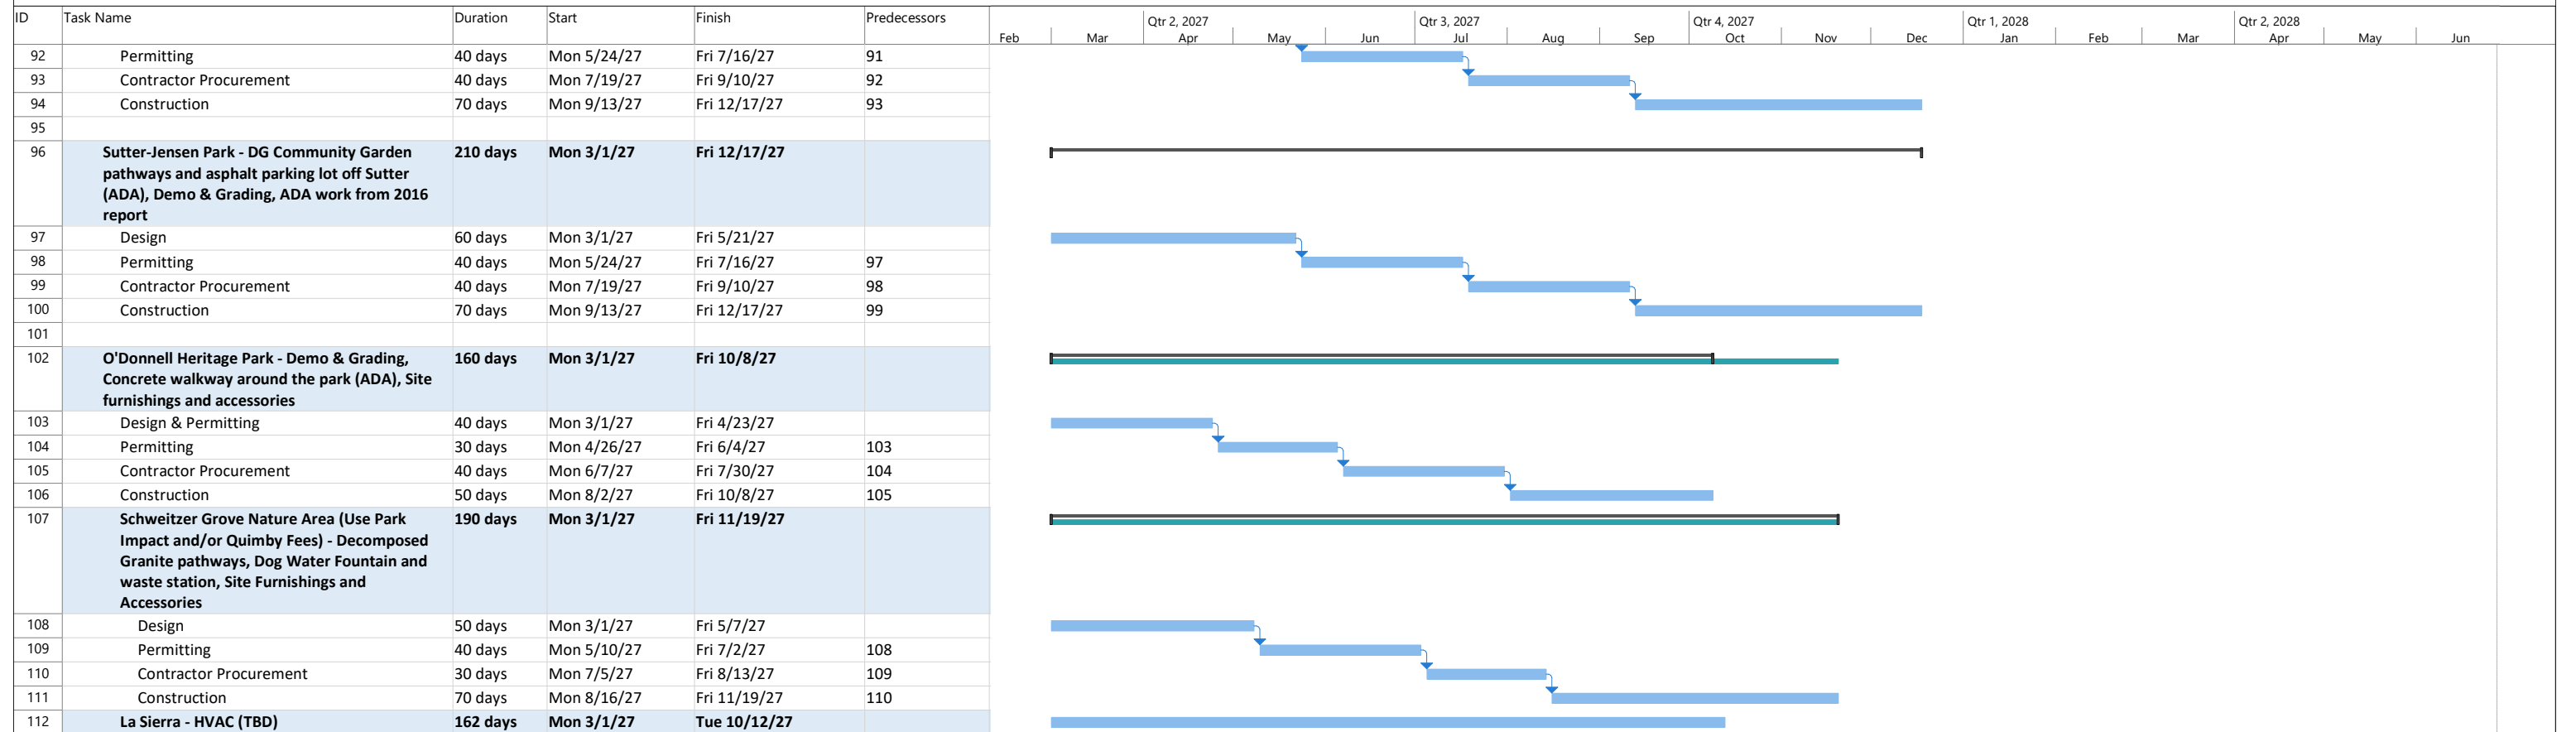

Project: Template_Schedule - A
Date: Wed 11/20/24

